

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 1 of 14

WARNING - PROPRIETARY RIGHTS NOTICE

This document is the property of Pratt & Whitney Canada Corp. ("P&WC"). You may not possess, use, copy or disclose this document or any information in it, for any purpose, including without limitation to design, manufacture, or repair material, or obtain FAA or other government approval to do so, without P&WC's express written permission. Neither receipt nor possession of this document alone, from any source, constitutes such permission. Possession, use, copying or disclosure by anyone without P&WC's express written permission is not authorized and may result in criminal or civil liability.

NOTICE - DISCLOSURE OF INFORMATION

This document contains trade secrets or other confidential information, the further disclosure of which may be harmful to Pratt & Whitney Canada Corp. If the head of a Government agency or department intends to disclose any of this information, written notice should be given to: the Vice President - Legal Services, Pratt & Whitney Canada Corp., 1000 Marie-Victorin (01BE5), Longueuil, Quebec J4G 1A1.

1.0 Revision History

Revision	Date	Nature of Changes
1.0	Feb 25th, 2025	7.1 (Program Health Dashboard repl by Program Health Monitoring)
Initial	Jan. 24th, 2019	Initial Release

	NAME	TITLE	DATE
Prepared by:	Branislav Vesic	Operations Program Analyst	November 26th, 2018
	Catherine Dugas	Operations Program Analyst	November 26th, 2018
	Lesley Grice	Operations Program Engineer	November 26th, 2018
	Michael Hepp	Operations Program Analyst	November 26th, 2018
	André Lemieux	Operations Program Analyst	November 26th, 2018
	Daniel Oboza	Operations Program Manager	November 26th, 2018
Approved by:	Etienne Ferland	Operations Program Manager	January 17th, 2019
	Maged Youssef	OPO Quality Associate Director	February 25th, 2025

☒ Original on file

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 2 of 14

TABLE OF CONTENTS

1.0	Revision History.....	1
2.0	Export Control Requirements	3
3.0	Scope and Purpose.....	3
4.0	Acronyms	3
5.0	Definitions	4
6.0	References	5
7.0	Introduction.....	6
7.1	Program Health Monitoring.....	7
7.2	Recurring Tasks	8
7.3	Legacy Program Annual Budget	8
7.4	Escape Management.....	8
7.5	OEM Management	9
7.6	Return engines	9
7.7	Consignment Hardware and Material Replacement	9
7.8	OEM Engine Upgrade Plan (OEUP)	9
7.9	Engine Downgrades.....	10
7.10	Change Order Activities	10
7.11	Resourcing and Cost Reduction Projects	10
8.0	Program Logistics	11
8.1	Special Schedule Engine Query (SSEQ) Process	11
8.2	Engine Schedule Request (ESR) Process	11
8.3	New Build Specification Creation.....	11
8.4	Program Restarts	12
8.5	Conversion of Production Engines	12
8.6	Program Termination.....	13

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025
	Legacy Program Management	Page 3 of 14

2.0 Export Control Requirements

To ensure compliance with current export control laws and regulations of the Canadian and U.S. governmental agencies regarding the export or transfer by any means, directly or indirectly, of any controlled goods or technical data, in accordance with MMP375, the reader shall refer to OPMP 7.1, OPM Compliance to Applicable Export Control Regulations.

In the event any data is received, created, handled or transferred during the execution of this procedure, it is the employees' responsibility to ensure all export control requirements are addressed, all data has been classified, and anyone with whom they are sharing the data, has the appropriate clearances.

In the event any clarifications or questions arise related to export control, the reader is requested to consult their departmental ITC focal.

3.0 Scope and Purpose

Operations Program Management (OPM) is dedicated to manage all aspects of Operations at a program level to ensure that the product meets or exceeds P&WC and customer needs and expectations. The scope of this procedure is to define the roles and responsibilities of OPM in the management of legacy programs within the Operations organization after Passport 4 approval and until program termination.

4.0 Acronyms

BOM	Bill of Material
BS	Build Specification
CO	Change Order
EASA	European Aviations Safety Agency
GWT	Global Work Transition
IPT	Integrated Product Team
KPI	Key Performance Indicators
OEM	Original Equipment Manufacturer
OEUP	Original Equipment Upgrade Plan
OPA	Operations Program Analyst
OPE	Operations Program Engineer

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 4 of 14

OPM	Operations Program Management
OPMP	Operations Program Management Procedure
OPR	Operations Programs Review
ORM	Operations Review Meeting
PCOR	Program Customer Operations Review
PMT	Program Management Team
PMMT	Program Model Management Team
QMSP	Quality Management System Procedure
QS&P	Quality Systems & Processes
RECO	Return Engine Change Order
RFN	Red Flag Notice
SAP	System Application Programming
SI&OP	Sales, Inventory and Operations Planning
SSEQ	Special Supply Chain Engine Query
TLM	Thursday Leadership Meeting

5.0 Definitions

Build Specification: A product definition document which provides the specific build configuration requirements and identification for an End Item, (consistent with engine model designation) for a particular customer.

Legacy Program: A program that is post Aircraft Entry into Service, or program for which start-up budget is closed or funded by inventory managed budget.

Manufacturing Approval: Engine Centre's first article inspection using a production engine to verify that all production processes, documentation, tooling and personnel are capable of producing engines that meet production requirements as per Transport Canada (TC), European Aviations Safety Agency (EASA) and Urząd Lotnictwa Cywilnego (ULC) - Civil Aviation Authority of the Republic of Poland.

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 5 of 14

Marketing Proposal Inquiry: Process raised to respond to customer requests for a new or derivative engine model or series. The MPI can be used in two instances: for a Request for Information, in an exploratory mode prior to Passport 0 and in a Request for Proposal (RFP) with more defined requirements, prior to Passport 1.

Demand Change Request (DCR): A request from P&WC Contract Administrator to Master Scheduling to evaluate schedule change proposal within period of 12 months. Converted to Engine Schedule Request (ESR) if Supply Chain input is required.

Engine Schedule Request (ESR): Master Scheduling request to Supply Chain and Engine Centre if schedule change can be supported from hardware availability and Engine Centre's capacity point of view. ESR shall be responded within 2 weeks from release date.

Special Schedule Engine Query (SSEQ): Treated as an ESR in case that less than four engines have been built in the past two years. SSEQ shall be responded within four weeks from release date.

Ship Short CO: Allows shipment of an engine with missing hardware (incomplete BOM) to ensure engines flow at OEM. This is approved by Marketing and Finance (P&WC 11365). When hardware becomes available it is shipped at final destination as per Marketing's request. (Ref. OPMP 5.10)

Rescind CO: Always accompanies a Ship Short CO to reintroduce the parts on the BOM of the specific short engine as soon as they become available. (Ref OPMP 5.10)

OEUP: An Original Engine Upgrade Plan is used to upgrade parts following a Change Order incorporation that is required to be introduced on engines already delivered at the OEM which have not received their Certificate of Airworthiness.

Escape: Raw material, parts, assemblies, engines and Integrated Power Plant System (IPPS) which do not meet specified requirements, which were or may have been released for further processing for incorporation into a higher assembly, a new or maintenance engine or for spare orders. (Ref. QMSP 08-03)

Production Engine: An engine that has received an Authorized Release Certificate confirming that subject engine conforms to approved design data and is in a condition for safe operation. Engine can therefore be used for service. (Ref. QMSP 08-03)

6.0 References

EOP 22	Limited Notice / Red Flag Notice
MMP 219	Integrated Product Management Process
MMP 220	Passport Review Process

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 6 of 14

MMP 300	Work Transition
MMP 444	Marketing Proposal Inquiries (MPI's)
OPMP 1.10	Program Management Communications
OPMP 2.10	OPM Annual Budget Management
OPMP 3.1	Coordinate Manufacturing Approval and Readiness Activities
OPMWI 3.11.6	Pre-Production engines Work Instructions
OPMWI 3.12.1	Program Restart Work Instructions
OPMWI 3.12.2	Escape Management Work Instructions
OPMWI 3.12.3	Engine Downgrades Work Instructions
OPMWI 3.12.4	Recurring Tasks and Reports Work Instructions
OPMP 4.11	Production Hardware Management
OPMP 4.12	OEM Hardware Management Procedure
OPMP 5.10	Change Order Incorporation Management Procedure
OPMWI 5.10.1	Change Order Incorporation Management / Red flag and Limit Notice Work Instructions
OPMP 6.10	Management of Delivered Engines Procedure
OPMWI 2.10.1	OPM Annual Budget Cycle
OPMPWI 6.10.1	OEM Return Engines
OPMWI 6.10.2	FPS Leasco Return Engines Work Instructions
OPMWI 6.10.3	Original Equipment Upgrade Plan (OEUP) Process Work Instructions
QMSP 08-03	Control of Non-conforming Product
QMSP 08-03-04	Red Flag Notice
QMSP 10-06	Manufacturing Approval
QMSP 10-07	Conversion of Production Engines
QMSP 10-08	Airworthiness Quality Plans

7.0 Introduction

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
		Date: Feb 25th 2025
Procedure Title	Legacy Program Management	Page 7 of 14

Operations Program Management (OPM) is dedicated to manage all aspects of Operations at a program level to meet and exceed customer needs and expectations through product performance excellence . OPM's raison d'être (purpose) is to ensure that Operations groups activities, projects and even resources are aligned with Customer, Market Segment and Programs strategies and needs. OPM function as shown in Figure 1: OPM "raison d'être" is the channel between Program Management Team stakeholders and Operations groups.

OPM's role is also being the Voice of Operations to the Program Management Team stakeholders at IPT / PMT / PMMT levels and even customers and OEM when required.

Therefore, it is OPM's mandate to ensure resolution of operations issues in a timely manner by collaborating with other key departments such as Supply Management, Engineering, Marketing, Aftermarket Customer Programs, Quality, etc., as per Integrated Product Management Process. (Ref. MMP 219).

From this Raison d'être, the OPE / OPA is responsible to understand program or customer issues, to establish the action path to resolution with the relevant Operations groups.

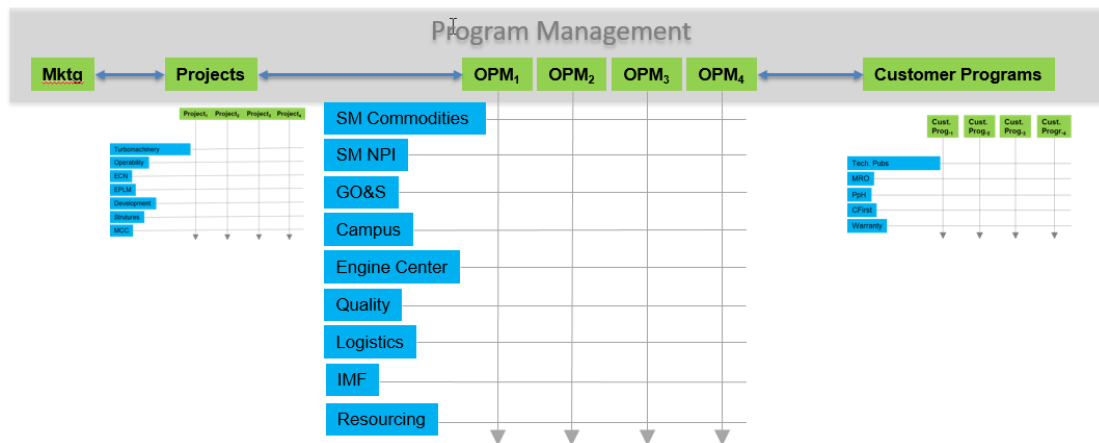


Figure 1: OPM "Raison d'Être"

7.1 Program Health Monitoring

Program Health Monitoring provides a comprehensive assessment of a program's overall health/performance by evaluating KPIs collected from various stakeholders, enabling OPM to use them for presentations requested by business leadership.

The KPIs are categorized into three main areas: Delivery, Quality, and Cost. They are measured throughout different stages of a program. These KPIs are reviewed periodically, with issues escalated and tracked through relevant forums within the program management process and structure (IPTs, PMTs, PMMTs, etc.)

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 8 of 14
	Legacy Program Management	

The OPE / OPA should understand these KPIs and customer needs to properly assess the impact and work with the accountable organizations to ensure risk management and recovery plans are in place, as well as launching and leading initiative IPTs where appropriate.

7.2 Recurring Tasks

Refer to Recurring Tasks and Reports Work Instructions (OPMWI 3.12.4) for the list of reports and tools available and the associated OPE / OPA's tasks and expectations.

7.3 Legacy Program Annual Budget

OPE / OPA is responsible to estimate following year legacy programs operations budget, based on the top Design Jobs funded by the PMT. Results are communicated to the OPM Budget Coordinator typically every second quarter of the year. (Ref. OPMP 2.10 / OPMWI 2.10.1)

7.4 Escape Management

The Escape Management process is initiated and led by Quality Managers or Project Engineers or respective delegates. It starts with a pre-escape meeting with the mandate to determine the risks and magnitude of the escape, to establish an appropriate plan of action for containment measures, to define root cause(s), correctives action(s) and to determine proper documentation to promptly address the problem. (Ref. QMSP 08-03-04)

The need for a RFN is determined during the escape management process:

- The Quality Red Flag Notice (RFN) is a mean to contain and maintain traceability of non-conforming product that has escaped the producer's quality system. The decision for issuing a RFN is determined by the Escape Management Process. (Ref. QMSP 08-03-04)
- If the non-conformity leads to an Engineering escape, Engineering will lead the RFN meeting (Ref. EOP 22). As a result, Engineering RFN drives to new design release and CO production incorporation. OPE / OPA's roles and responsibilities are defined in OPMP 5.10 CO Incorporation Management procedure.

During the Escape Management meeting (EMM), OPE / OPA represents Operations and OEM and helps in part containment by providing the necessary information to EMM leader which is captured in EMM Minutes (Ref. PWC Form 10254). In addition, OPE / OPA engagement at the OEM supports engines upgrade program and end items upgrade or replacement. This process is applicable prior to the aircraft receiving the Certificate of Airworthiness.

Additional OPE / OPA responsibilities include:

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 9 of 14

- Non-conforming product replacement at the OEM in collaboration with P&WC Field Service Representative (FSR);
- Leads engine upgrade program at the OEM when CO allows hardware replacement at the OEM, or subcontracts OEM product upgrade to Mobile Repair Team (MRT) (Ref. OPMP 6.10);
- Coordinate return engine upgrade program with Engine Centre if required.

7.5 OEM Management

Support of delivered engines and end items at the Original Equipment Manufacturer (OEM) final assembly line is managed by OPM until the aircraft ownership transfer to end-user and Certificate of Airworthiness issuance. The contract with the customer, the location and on-site support will influence the support provided by OPM. OPM is involved in coordinating logistic tasks including material and manpower required to support the OEM.

7.6 Return engines

The management by OPM for return engines will be determined by the program and may depend on the type of activity driving the return (planned or unplanned returns). Once a requirement is established, the OPE / OPA will coordinate the plan with Marketing and the Engine Centre. For return engines requiring an OEUP, OPM will support the review of the material planning. (Ref. OPMP 6.10; OPMWI 6.10.1 & 6.10.2)

7.7 Consignment Hardware and Material Replacement

The objective of consignment is to have hardware available on-site at the OEM for immediate use by OEM Final Assembly Line (FAL). Quality issues, technical issues or experience from other programs are used to determine the requirements. In the case that a part is being recalled to be used otherwise, it has to be replaced at first opportunity by the FSR of the OEM advised. For OPE / OPA roles and responsibilities associated with consignment stock and material replacement management are defined in OPMP 4.12 - OEM Hardware Management procedure.

7.8 OEM Engine Upgrade Plan (OEUP)

Engineering or Marketing advises OPM of an OEUP requirement. Once advised, the OPE / OPA chairs the Logistics Plan Meeting to formalize the scope of work, timeline and plan for the OEUP (Ref. OPMP 6.10 and OPMWI 6.10.3). This activity should be done in collaboration with the OEM FSR. The OPE / OPA is also responsible to provide an update in the OEUP Upcoming Retrofit report upon reception of email by Cyient.

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 10 of 14
	Legacy Program Management	

7.9 Engine Downgrades

In some instances a production engine may need to be downgraded from production to experimental status in the situations listed below:

- Customer request for flight or ground testing with some engine components including software not already approved per the Bill of Material, or for testing intended to be operated outside the normal operating limits;
- Engineering request for the downgrade of production engines to be converted to a new derivative configuration, or installation of non-production components for testing at the customer (i.e. Customer Engine);
- Operations request due to a critical part shortage, the customer may request flightworthy production engine that includes flightworthy non-production standard part(s).

In all cases listed above, an Airworthiness Quality Plan (AQP) is issued to control uncertified engines, to ensure that they will remain certifiable as production engines (Ref. QMSP 10-08).

Depending on the situation above, OPE / OPA's mandate is to lead or participate in the IPT during downgrade and upgrade processes (Ref. OPMWI 3.12.3).

7.10 Change Order Activities

OPM's objective is to strive for on-time production incorporation delivery of the Change Order (CO) to meet Program commitments. OPE / OPA's responsibility is to coordinate all activities required for implementation of a new CO including Operations business units, suppliers, internal manufacturing and Engine Centre readiness. OPE / OPA needs to ensure that the key stakeholders are aligned with the CO release and incorporation strategy (Ref. OPMP 5.10 and OPMWI 5.10.1) with OPM being responsible for participating in IPTs, raising Change Requests (CR) to accommodate Operations' day-to-day needs and CO approval.

OPE / OPA is reporting the progress of the CO release and incorporation plan to PMT / PMMT. However, OPE / OPA has a responsibility to report any deviation to Engineering-directed or customer committed CO production incorporation plan. Issue must be presented and reviewed by the PMT and subsequently presented to PMMT in case of commitment change. In addition, review platforms such as the Strategic and Operational PCORs can be used to emphasize PMMT objectives. They can also serve as a flow down platform to the Operations team with the purpose of highlighting support needed and the importance of the task.

7.11 Resourcing and Cost Reduction Projects

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 11 of 14
	Legacy Program Management	

OPM role is to be informed about resourcing projects, understand impact on engine program, and help and guide if necessary. OPM is not part of the approval process of resourcing projects. Under the governance of MMP300, Global Work Transition (GWT) team is the resourcing process owner.

OPE / OPA engagement starts at the Pre-Gate A where OPM resourcing lead is invited by the GWT IPT leader to attend start-up IPT. As a result, OPM is informed about the project, affected hardware and schedule. Based on that, OPM resourcing lead communicates resourcing activity to affected Engine Program OPM team.

OPE / OPA's mandate is to ensure that Engine Program PMT's and GWT IPT's production incorporation targets are aligned and that there is no interference between two groups' production incorporation plans. In case that interference exists, it would be OPE / OPA's responsibility to present findings to Engine Program PMT and to GWT IPT and request schedule adjustment. OPE / OPA liaison function between Engine Program PMT and GWT IPT shall cease upon resourcing project completion.

In addition, resourcing activity and impact to engine program and FSC will be presented through Program Health Dashboard.

8.0 Program Logistics

8.1 Special Schedule Engine Query (SSEQ) Process

As described in definition section, OPE / OPA is receiving SSEQ request from Accenture via email and request shall be answered before defined due date. OPM to provide YES / NO (with proposed pushout dates) answer and comments in the request based on the following input:

- Manufacturing approval required and associated budget and capacity;
- Incorporated and pending release CO that could impact engine production;
- As a best practice, it is recommended to avoid last quarter of the year in order to minimize impact and risk on year-end deliveries.

8.2 Engine Schedule Request (ESR) Process

Engine Schedule Request is a process managed by Master Scheduling and distributed by Accenture. OPE / OPA is responsible to review ESR and assess if schedule change affects Change Order (CO) production incorporation strategies and escalate to OPM / SI&OP Management if required. On occasions when ESR is rejected, OPE / OPA should evaluate possible strategies to support product sales.

8.3 New Build Specification Creation

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 12 of 14
	Legacy Program Management	

A need for new Build Specification (BS) is flown down to Program PMT via Marketing Proposal Inquiry (MPI). The OPM Manager and / or OPE / OPA attends the Marketing kick-off meeting for MPI proposal to obtain new program specifications, including any contractual obligations and delivery schedule. For detailed OPE / OPA responsibilities refer to procedures OPMP 3.10 Industrialization - Pre-Passport 0 up to Passport 2 and OPMP 3.11 Industrialization - Passport 2 up to Entry into service.

In some rare occasions, a new BS should be requested by OEM or by P&WC Marketing under the condition that new BS Manufacturing Bill of Material (mBOM) is the same as current production one, and the only difference is delay of production incorporations between two BS by period specified by OEM. In that case OPE / OPA shall request new BS release to production (Ref. OPMP 3.11). Upon CO release, OPE / OPA requests new BS to be loaded in SAP and requests from Marketing and Master Scheduling to split demands between production and spares deliveries.

8.4 Program Restarts

When a previously-approved engine model is out-of-production for more than two years and the applicable Engine Centre is required to resume production, the Manufacturing Approval process shall be repeated. The OPE / OPA is responsible for procedural compliance to QMSP 10-06 and OPMP 3.1 by initiating and leading Manufacturing Approval IPT until engine delivery. An SSEQ request will be required and will usually be the signal to launch the Restart process.

8.5 Conversion of Production Engines

Production engine conversion is a process where engine could be converted from one build specification to another, or one engine model to another. This process is not applicable for uncertified engines or engines installed on an aircraft with Certificate of Airworthiness (C of A) or Export C of A. A Changer Order (CO) that contains instructions for the conversion of an engine is required when the engine has been released with an Authorized Release Certificate (ARC) and has been delivered to the OEM / Customer except for "P&WC Leasing".

Conversion CO is not required if the engine is still within P&WC Manufacturing premises (not delivered to OEM) which includes conversion prior ARC release, conversion from one build specification to another within same engine model and conversion from one engine model to another after being shipped to FPS or P&WC Leasing.

For more details refer to QMSP 10-07 - Conversion of Production Engines.

OPE / OPA responsibility in production engines conversion process includes:

1. Full compliance to QMSP 10-07;

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 13 of 14

2. OPE / OPA to request and review copy of the RECO file from Cyient;
3. Validate RECO CO compliance code;
4. Present findings to IPT / PMT and request Engineering / Aftermarket compliance to CO incorporation plan proposal;
5. Validate Engine Centre production readiness and Manufacturing Approval status for required engine model;
6. Validate with Quality Performance or Engineering if any red flag or quality escape may apply to the conversion engine model;
7. Coordinate return engine process (Ref. OPMP 6.10, OPMWI 6.10.1 and 6.10.2).

8.6 Program Termination

Driven by business decision or other factors, OEM may elect to terminate engine program and request a contract cancellation to P&WC.

Program Termination process is managed by Marketing, Communications, Legal, Master Scheduling, SI&OP and Supply Management teams. Termination of product deliveries to OEM is not a termination to our suppliers and partners. Communications, Legal departments and Supply Chain are responsible to flow down information to unique hardware suppliers with a purpose to reiterate their obligation to support field engine (Aftermarket sales). Common hardware suppliers are not informed about termination and process is managed by demand reduction process by Supply Chain.

In above-mentioned process, OPM does not have authorization to discuss program termination with suppliers, authorize stock or tooling scrap.

When instructed by program PMMT / PCOR / PMT about program termination, OPE / OPA's responsibilities are as follows:

- Engines that never entered into service:
 - Strip engine and return parts to stores (Ref. OPMP 4.11);
 - Convert to other engine model for P&WC Leasing use (Ref. OPMP 6.10).
- Engines passed entry into service:
 - Excess engines owned by P&WC Leasing and conversion request submitted to OPM (Ref. OPMP 6.10).
- NOP demands for unique hardware for terminated program:

 Pratt & Whitney Canada Une société de United Technologies / A United Technologies Company	Operations Programs Management Procedure	OPMP: 3.12 Rev.: 1.0
Procedure Title		Date: Feb 25th 2025 Page 14 of 14
	Legacy Program Management	

- Work closely with Supply Chain to remove hardware demands.
- Risk orders and NOP demands (Ref. OPMP 4.11):
 - Inform Supply Chain of intent to cancel Risk Order(s) and / or NOP Purchase Order(s);
 - Request Risk Order and NOP P.O. cancellation;
 - Supply Chain Account Specialist to cancel P.O.;
 - OPM Planner to remove Purchase Requisition;
 - Request Risk Order Internal Order (IO) cancellation including WBS from OPM Finance.
- Review program Change Orders (pending release, released but not incorporated into production and Pink CO's) and facilitate transition plan as per Program PMT disposition.
- Managed budget:
 - Work with OPM Finance to cancel managed budget for terminated engine program.
