WARNING - PROPRIETARY RIGHTS NOTICE

This document is the property of Pratt & Whitney Canada Corp. ("P&WC"). You may not possess, use, copy or disclose this document or any information in it, for any purpose, including without limitation to design, manufacture, or repair material, or obtain FAA or other government approval to do so, without P&WC's express written permission. Neither receipt nor possession of this document alone, from any source, constitutes such permission. Possession, use, copying or disclosure by anyone without P&WC's express written permission is not authorized and may result in criminal or civil liability.

NOTICE - DISCLOSURE OF INFORMATION

This document contains trade secrets or other confidential information, the further disclosure of which may be harmful to Pratt & Whitney Canada Corp. If the head of a Government agency or department intends to disclose any of this information, written notice should be given to: the Vice President - Legal Services, Pratt & Whitney Canada Corp., 1000 Marie-Victorin (01BE5), Longueuil, Quebec J4G 1A1.

1.0 Revision History

REVISION	DATE	NATURE OF CHANGES
1.0	February 28th, 2018	Sections added to cover: OPMP 1.2, 1.3, 1.4, 1.6, 2.1, 2.2, 2.3 and includes their intent
Initial	May 31, 2016	Initial release. Obsoletes OPMP 1.1 and 1.5 includes their intent

	NAME	TITLE	DATE
Prepared by:	**Chantale St-Arneault**	**Operations Program Engineer**	**Feb 28, 2018**
	Roxane Medeiros	**Operations Program Engineer**	**Feb 28, 2018**
	Michelle Brunelle	**Special Projects Coordinator**	**Feb 28, 2018**
Approved by:	**Dominique Di Iorio**	**Operations Program Manager**	**Feb 28, 2018**

☐ Original on file

TABLE OF CONTENTS

1.0 Revision History 1

2.0 Export Control Requirements 4

3.0 Scope 4

4.0 Acronyms 4

5.0 Definitions 5

6.0 References 6

7.0 Pre-Passport 0 7

- **7.1 NPI Operations Budget** 7
  - **7.1.1 Request for Information** 7
  - **7.1.2 OPM Responsibilities during RFI** 7
- **7.2 Engine FSC** 8
- **7.3 Sourcing and Manufacturing Strategy** 8
  - **7.3.1 Advanced Program Sourcing** 9
  - **7.3.2 Dual Sourcing** 10
- **7.4 Program Operations Risks Management** 10
- **7.5 Program Level 1 Plan** 10

8.0 Passport 0 to Passport 1 11

- **8.1 NPI Operations Budget** 11
  - **8.1.1 Request for Proposal** 12
  - **8.1.2 OPM Responsibilities during RFP** 12
- **8.2 Engine FSC** 13
- **8.3 Sourcing & Manufacturing Strategy** 13
  - **8.3.1 Advanced Program Sourcing** 14
  - **8.3.2 Dual Sourcing** 14
- **8.4 Program Operations Risks Management** 15
- **8.5 Program Operations Level 1 & 2 Plan** 15

9.0 Passport 1 to Passport 2 16

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

9.1 NPI Operations Budget 16

9.2 Engine FSC 16

9.3 Sourcing & Manufacturing Strategy 16

9.4 Program Operations Risks Management 17

9.5 Program Operations Level 1 & 2 Plan 17

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

2.0 Export Control Requirements

To ensure compliance with current export control laws and regulations of the Canadian and U.S. governmental agencies regarding the export or transfer by any means, directly or indirectly, of any controlled goods or technical data, in accordance with MMP375, the reader shall refer to OPMP 7.1, OPM Compliance to Applicable Export Control Regulations.

In the event any data is received, created, handled or transferred during the execution of this procedure, it is the employees' responsibility to ensure all export control requirements are addressed, all data has been classified, and anyone with whom they are sharing the data, has the appropriate clearances.

In the event any clarifications or questions arise related to export control, the reader is requested to consult their departmental ITC focal.

3.0 Scope

The scope of this procedure is to describe Operations Program Management (OPM) role in achieving a successful industrialization of a new program. OPM is responsible for Production readiness process for the transition of components, engines (including APUs) and powerplants from Marketing proposal through serial production (MMP 219, MMP 220). OPM strives for each program to ensure delivery a producible product that is sourced to meet program objectives of cost, yield, quality, schedule and Change Order effectivity.

As soon as an MPI request is raised by Marketing to study a new Program, OPM takes an active role in defining: the NPI Operations Budget, the Program sourcing strategy and risks, the Level 2 Operations plan and the Operations' PDRS. This procedure defines the roles and responsibilities of OPM during this industrialization planning phase.

Note: For program re-start or IPPS, the OPE / OPA can apply the following activities when deemed necessary.

4.0 Acronyms

CAR	Capital Acquisition Request
CBN	Cost Basis Note
CDR	Critical Design Review
DPM	Digital Product Management
EIS	Entry Into Service

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

FER	First Engine Run
FSC	Factory Standard Cost
I.Os	Internal Orders
LLT	Long Lead Time
MPI	Marketing Proposal Inquiry
NPI	New Product Introduction
NRE	Non-Recurring Expenses
OEM	Original Equipment Manufacturer
OPE	Operations Program Engineer
OPA	Operations Program Analyst
PDR	Preliminary Design Review
PDRS	Product Design Requirement Specifications
RFI	Request for Information
RFP	Request for Proposal
ROM	Rough order of magnitude
SFV	Strategic Financial Valuation
UPPAP	United Technologies Production Part Approval Process

5.0 Definitions

Investment Audit: Regular financial exercise that compares the latest estimates of projected spending, cash flows and other program benefits against the original assumptions set forth in the capital appropriation request.

Program Industrialization Phase: Starts with Passport 0 - Permission to study and ends with Passport 4 - Permission to Deliver Serial Production, and / or Aircraft Entry Into Service.

Marketing Proposal Inquiry: Raised to respond to customer requests for a new or derivative engine model. The MPI can be used in two instances: for an RFI, in an exploratory mode prior to Passport 0 and in an RFP with more defined requirements, prior to Passport 1 - Permission to Offer.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

Key Component: Is a part unique to the program which has one or more of the following characteristics: high complexity, high cost, long lead time, new supplier, new technology, dual sourced, etc... (ref. complete list of characteristics in OPMP 5.10 Change Order Management).

Contractual Obligations: Include various obligations such as Offset obligations as defined by Marketing in the contract with the OEM, Partnership with revenue sharing and joint ventures, and any obligations with governments resulting from project funding agreements.

6.0 References

EOP 60	Management of Product Development Program
MMP 219	Integrated Product Management Process
MMP 220	Passport Review Process
MMP 348	Sourcing
MMP 444	Marketing Proposal Inquiries (MPI's)
MMP 501	New Product Introduction FSC Management
MMP 911	Business Continuity Management (Part of dual sourcing and risk management)
OPM Budgeting and Cost Collection Guide	
OPMWI 3.10.1	Establish and Maintain NPI Operations Budget
OPMWI 3.10.2	Review and Validate Program Sourcing
OPMWI 3.10.3	Manage Program Operations Risks
OPMWI 3.10.4	Establish Program Operations Level 1 & 2 Plan
P&WC 11847	NPI Operations Budget form
P&WC 11895	Program Sourcing Strategy form
P&WC 11908	Dual sourcing & Single point of failure decision matrix form
Program Operations Level 1 and 2 Plan template	
Program Operations Risks template	
Sourcing Strategy Meeting template	

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

7.0 Pre-Passport 0

Following a customer inquiry, Marketing raises a Marketing Proposal Inquiry (MPI) to gather from various organizations the required information to support a proposal. OPM's roles and responsibilities during that phase are listed in the following sections. The OPE / OPA shall charge any related Operations activity to the Advanced Engineering I.O.

7.1 NPI Operations Budget

In response to a Marketing Proposal Inquiry (MMP 444), OPM is responsible to establish a NPI Operations Budget that captures all funds required by Operations to industrialize a new program. The purpose of this section is to ensure that a consistent approach is used to enable the delivery of a complete and timely response.

Note: Please refer to OPMWI 3.10.1 Establish and Maintain NPI Operations Budget for details.

7.1.1 Request for Information

The OPM Manager and / or Operations Program Engineer (OPE) / Operations Program Analyst (OPA) attend the Marketing kick-off meeting for MPI proposal to obtain new program specifications, including any contractual obligations. All organizations must agree on a schedule for providing a response. Depending on program scope, the completion of NPI Ops. Budget typically takes from 4 to 6 weeks.

Before launching any activities, a technical solution (Engine only or Engine and IPPS) shall be obtained from Engineering including the Level 1 Plan (EOP 60). At this Passport stage, the technical solution is typically high level and should be conveyed through a preliminary cross-section.

The level of accuracy expected following a MPI request will depend on the nature of the customer inquiry (RFI vs RFP). Prior Passport 0 and / or for RFI's, rough order of magnitude (ROM) are considered acceptable.

7.1.2 OPM Responsibilities during RFI

The OPE / OPA is responsible to provide inputs on the following three aspects:

1. Based on the program scope, evaluate resources and funding required to support program activities including OPM resources, Manufacturing Approval (Engine only), 3P events and travel.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

2. For a new **centerline**, validate the Sourcing strategy assumptions which are part of the Cost Basis Note (CBN) generated by the Product Cost group. For a **derivative**, as a minimum, verify the impact of a significant volume increase and high level sourcing strategy defined in the CBN. Detailed sourcing strategy validation can be postponed to Passport 1 - Permission to offer. Please refer to section 7.3 below for more details.

3. Obtain from each Manufacturing Unit and Engine Centre, estimates on buildings, machines, tooling and NRE required to support the industrialization of the program. NPI Quality organization will supply United Technologies Production Part Approval Process (UPPAP) estimates (parts and engine), DPM will evaluate Change Incorporation Analyst (CIA) scope of work and Customer Engineering will provide an estimate on OEM Toolings.

Managed and capital charges shall be entered in the NPI Operations Budget form (P&WC 11847). Background justifications must be included to facilitate traceability throughout the program lifecycle.

It is recommended, before finalizing the NPI Ops. Budget form, to review the Engineering Cost Estimate (ECE) to ensure that all tools required are properly allocated between Engineering and Operations budgets.

Once reviewed by the OPM Manager, the completed NPI Ops. Budget form is provided to Strategic Financial Valuation (SFV) and Marketing organizations.

7.2 Engine FSC

Prior Passport 0, a ROM CBN is generated by the Product Cost group based on the proposed engine architecture. The OPE / OPA typically needs to validate the associated sourcing assumptions with the support of Engineering, Procurement and Strategic Sourcing (refer to next section for details). If at this stage, a gap is identified between the ROM CBN (which includes the FSC targets) and the business case target, the OPM Manager elaborates a plan to influence sourcing strategy and design complexity in order to meet cost targets.

Note: Refer to MMP 501 New Product Introduction FSC Management for more details.

7.3 Sourcing and Manufacturing Strategy

Establishing the sourcing and manufacturing strategy of a new program is critical to meet program objectives of cost, yield, quality and schedule. The OPE / OPA shall drive activities to review, validate, influence and achieve agreement on the program sourcing strategy with all stakeholders.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

Always ensure compliance with all Contractual obligations associated to the program and to ITC restrictions.

Note: Please refer to OPMWI 3.10.2 Review and validate Program Sourcing for detailed instructions.

7.3.1 Advanced Program Sourcing

Advanced Program Sourcing consists of defining the prime sources of a new program for engine build and test location and components procurement.

For the engine build and test sourcing strategy, OPM organizes a meeting with all stakeholders to determine the location where the new engine will be assembled and tested. At the same meeting, the decision whether or not sub-assemblies Assembly Method Document (AMD) are needed and where they will be sourced is taken. Dual sourcing needs are also discussed and agreed upon. Criteria that can drive this decision are capacity, overall manufacturing strategy, OEM requirements, etc..

For components (or parts) of the engine, and in order to establish the FSC baseline in the CBN, the Product Cost group identifies the most likely sources based on current sourcing of similar products for other programs.

The OPE / OPA organizes a meeting with the stakeholders to review and validate the basic program sourcing strategy of the Key Components (refer to OPMP 5.10 for complete list of characteristics) using the sourcing template and the form P&WC 11895 Program Sourcing Strategy Sheet.

The main objectives are:

1. Demonstrate compliance to Contractual obligations and Partnerships;

2. Ensure alignment with the Strategic Sourcing Review Board (SSRB) taking into consideration specific corporate objectives;

3. Evaluate any operational risks associated with the proposed sourcing based on MFA from other programs. Influence or challenge sourcing strategy in order to meet cost, delivery or quality of parts, and find alternatives or mitigation plans when necessary (refer to Risk Management section).

For a new centerline, this analysis is required for Passport 0 whereas for a derivative engine the validation can be postponed to Passport 1.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

7.3.2 Dual Sourcing

A dual sourcing strategy always needs to be assessed and evaluated in order to protect the program.

For the engine build and test location, please refer to previous section where dual sourcing is evaluated at the same time as Advanced Program Sourcing.

At the component level, the study will target certain part families (e.g. bearings, seals, complex castings, critical rotating forgings and turbine blades) per MMP 348. For a new centerline, the OPE / OPA organizes a meeting with all stakeholders to define and recommend a Components Program Dual Sourcing Strategy (ref. form P&WC 11908). For a derivative engine, a ROM can be established based on MFA from Supply Chain and Engineering. Results are recorded in form P&WC 11895 - Program Sourcing Strategy Sheet.

The component dual sourcing investments required for a derivative or new centerline program are included in the ECE. Final decision will be taken at Passport 1.

7.4 Program Operations Risks Management

Identifying operational risks early in a program is key to allow proper planning, control and timely decision making to meet customer commitments. Throughout the life of the program, the OPE / OPA drives the process of identifying and assessing risks, establishing mitigation plans and driving actions to closure.

For a new centerline prior Passport 0, identification of risks and mitigation plans is started during the Program Strategic Sourcing meeting with the input received from Operations Strategy, Manufacturing units, Engineering and Supply Chain. The OPE / OPA also requests feedback from the Producibility group and Engine Centre. All operational risks are consolidated into a single file and evaluated in terms of likelihood and impact. The top operational risks are fed into the Program Risk Cube managed by Engineering. The OPE / OPA monitors and update the list of risks throughout the life of the program ensuring to drive mitigation actions to closure.

In case of a derivative engine, the same process is followed. However feedback from Operations Strategy, Engineering and Supply Chain is obtained on an individual basis since there is no Program Strategic Sourcing meeting held.

Note: Please refer to OPMWI 3.10.3 Manage Program Operations Risks for details.

7.5 Program Level 1 Plan

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

At this early stage, the OPE / OPA reviews and validates the Program Level 1 Plan created by Engineering (refer to EOP 60 for more information), adds the critical Operations' milestones and ensures that there is sufficient time allocated between milestones.

In the eventuality that the time between milestones is compressed, the OPE / OPA needs to understand the program scope, design complexities, lead time of Key Components, to ensure these risks are highlighted in the Program Risk Cube (see next section). Refer to typical Program Level 1 Plan in **Figure 1** below.

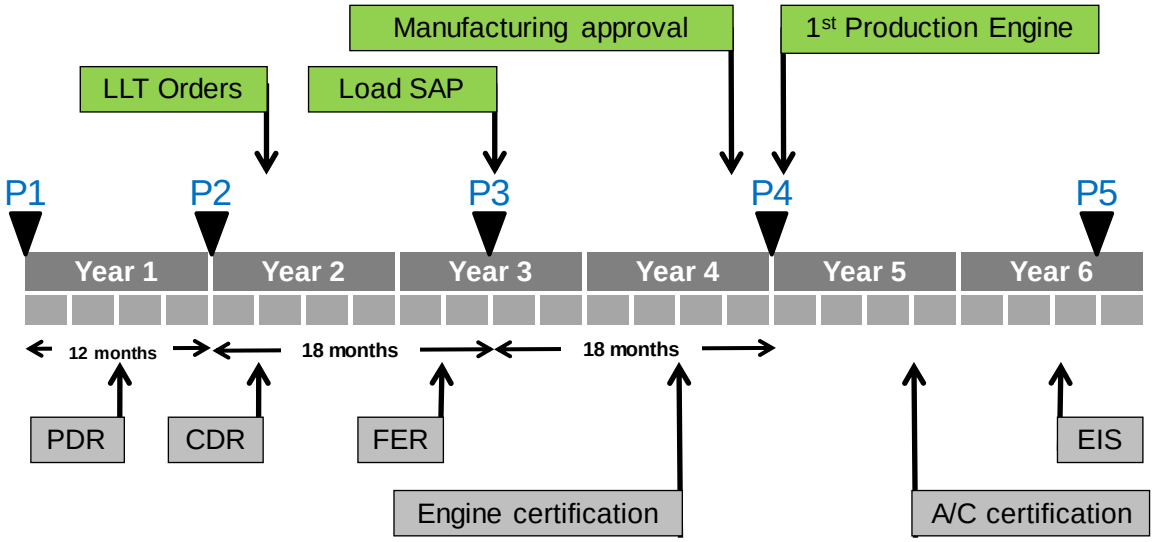

Figure 1 - Typical Program L1 Plan with Operations (Green) and Engineering (Grey) Milestones

8.0 Passport 0 to Passport 1

Marketing can decide to proceed with Passport 0 - Permission to study, after comparing the preliminary business case and the customer's expectations. Once Passport 0 is granted, it permits allocation of resources to refine technical solution resulting in more accurate business case. The OPE / OPA shall charge any related Operations activity to the Advanced Engineering I.O.

8.1 NPI Operations Budget

The OPM Manager and / or OPE / OPA attend the Marketing kick-off meeting for MPI proposal to understand if there are new program specifications, including any contractual obligations.

Note: Please refer to OPMWI 3.10.1 Establish and Maintain NPI Operations Budget for details.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

8.1.1 Request for Proposal

Marketing shall hold a kick-off meeting for MPI proposal to communicate status of the inquiry and agree on a schedule for providing a refined response. OPM's participation is required. Depending on program scope, the completion of NPI Ops Budget typically takes from 4 to 6 weeks.

8.1.2 OPM Responsibilities during RFP

Activities required to provide Operations' response to MPI are similar to those specified in Pre-Passport 0 (section 7.1), although a higher level of accuracy is expected after Passport 0 as shown in Table 1.

Initial estimates from Pre-Passport 0 need to be re-validated and assumptions well stated based on a more detailed Engineering Technical Solution (Engine only or Engine and IPPS).

Note that for a derivative, the sourcing strategy validation is done at this stage and for a new centerline, it is reviewed. NPI Ops. Budget form needs to go through signature cycle for approval. Once approved, signed copy is provided to SFV and Marketing.

Table 1: OPM Responsibities for MPI various responses

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

Activity	Pre-Passport 0 (RFI)	Passport 0 to Passport 1 (RFP)
Marketing kick-off meeting	Obtain volumes, technical solution and timeline	
Engineering Technical Solution	Obtain draft cross-section	
Supply Chain Capacity	Validate	
Sourcing Strategy	Validate for centerline	Review for centerline Validate for derivative
Dual Sourcing Strategy	Establish	Review
Equipment / Tooling **Manufacturing Units** **Engine Centres** **OEM**	Establish Capital	Review Capital
Managed **OPM** **DPM** **Process Planning** **UPPAP - Parts** **UPPAP - Engine**	Establish Managed	Review
Approval	OPM Manager	Obtain all required signatures

8.2 Engine FSC

An updated CBN is generated by the Product Cost group based on the latest engine architecture. The OPE / OPA needs to validate the associated sourcing assumptions with the support of Engineering, Procurement and Strategic Sourcing (refer to next section for details). If at this stage a gap between the CBN (which includes the FSC targets) and the business case target is identified, the OPM Manager elaborates a plan to influence sourcing strategy and design complexity in order to meet cost targets.

Note: Refer to MMP 501 New Product Introduction FSC Management for more details.

8.3 Sourcing & Manufacturing Strategy

In preparation for Passport 1, the OPE / OPA drives activities to re-validate the Sourcing Strategy established at Passport 0 with all stakeholders. The re-validation considers the more refined

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

Engineering Technical Solution, the business case requirements as well as the possible changes in Contractual obligations or introduction of a Partnership.

Always ensure compliance with all Contractual obligations associated to the program and to ITC restrictions.

Note: Please refer to OPMWI 3.10.2 Review and validate Program Sourcing for detailed instructions.

8.3.1 Advanced Program Sourcing

At the engine build and test level, the OPE / OPA re-confirms the strategy as established at Passport 0 with Engine Centre representatives.

For components (or parts) of the engine, the OPE / OPA organizes a meeting with all stakeholders to review and validate the associated sourcing strategy using the same process as explained in section 7.3 (refer to Table 2 below). Results are recorded in form P&WC 11895.

8.3.2 Dual Sourcing

The OPE / OPA re-confirms the engine dual sourcing strategy as established at Passport 0 with Engine Centre representatives.

The OPE / OPA organizes a meeting with all stakeholders to review the Components Dual Sourcing Strategy established for Passport 0 as shown in Table 2 below.

For a **new centerline**, the team recommendations documented in the Dual Sourcing Strategy are reviewed, corrected and reconfirmed using form P&WC 11908. For a **derivative engine**, a dual sourcing meeting needs to be scheduled (see section 7) as only a ROM was provided at Passport 0. Results are consigned in form P&WC 11895.

The dual sourcing investments required for a derivative or new centerline program are included in the ECE. Final decision will be taken at Passport 1.

Table 2: OPM Responsibities for Program and Dual Sourcing Strategies

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

	Derivative engine		New Centerline	
	Program Sourcing Strategy (P&WC 11895)			
	Advanced Program Sourcing	Dual Sourcing	Advanced Program Sourcing	Dual Sourcing
Passport 0 ***Permission to Study***	Use CBN sourcing	Evaluate	Validate CBN sourcing	Evaluate
Passport 1 ***Permission to Offer***	Validate	Review	Review	
Passport 2 ***Permission to Continue Detail Design***	Review if needed		Review if needed	
	Component Strategy (P&WC 10367)			
Passport 3 & up ***Permission to Order Serial Production***	Review if needed			

8.4 Program Operations Risks Management

For a new centerline and derivative engine, the OPE / OPA reviews the Program Operations Risks list established at Passport 0 with Engineering, Operations Strategy, Manufacturing units and Strategic Sourcing during the Program Strategic Sourcing meeting, by taking into account the latest technical definition and associated sourcing.

Feedback from Producibility group and Engine Centre is also required.

All operational risks are updated in the Program Ops. Risks list and evaluated in terms of likelihood and impact. The top operational risks are fed into the Program Risk Cube managed by Engineering. The OPE / OPA monitors and update the Program Ops. Risks list throughout the life of the program ensuring to drive mitigation actions to closure.

Note: Please refer to OPMWI 3.10.3 Manage Program Operations Risks for details.

8.5 Program Operations Level 1 & 2 Plan

The Program Operations Level 1 & 2 Plan identifies the key Operations' deliverables and decision points. It schedules them based on program and customer commit dates as they relate to the introduction of a new engine or derivative. The OPE / OPA uses the Program Operations template (MS Project) to create and maintain the Plan. At this stage of the program, only the Operations Level 1 Plan is required.

Note: Please refer to OPMWI 3.10.4 Establish Program Operations Level 1 & 2 Plan for details.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

9.0 Passport 1 to Passport 2

P&WC President's Office (Team 1) can decide to grant Passport 1 - Permission to offer, after review of the business case and customer's expectations. This will enable the submission of a technical and commercial proposal to the customer. Starting at Passport 1, the OPE / OPA shall charge any related Operations activity to OPM only Managed I.O.

9.1 NPI Operations Budget

After Passport 1 and upon customer contract agreement, SFV initiates the Program CAR. The OPE / OPA contacts the OPM Unit Accountant to obtain the OPM ONLY Managed I.O. This I.O. captures time spent by OPM resources to support the new program until closure of the NPI Ops. budget. Validation of the NPI Ops. Budget form will be requested at each Passport and investment audit. In order to prepare for these reviews, update form with actual spend, re-validate all estimates for future activities and add justifications if there are significant differences (+ 10%). A full re-approval signature cycle may be required. At this stage the completion of NPI Ops. Budget typically takes from 2 to 4 weeks.

Note: Please refer to OPMWI 3.10.1 Establish and Maintain the NPI Operations Budget for details.

9.2 Engine FSC

In order to carefully managed the engine FSC evolution, the Cost Project Engineer organizes regular Cost IPTs. The objectives are to action cost reduction initiatives and orient technical and commercial decisions towards achieving the engine FSC business case target as established in the CBN. As an active member of this IPT, the OPE / OPA is responsible to oversee the execution of the specific product component strategies to achieve the Procurement, Sourcing, Manufacturing and Engine Centre groups cost targets.

Note: Refer to MMP 501 New Product Introduction FSC Management for more details.

9.3 Sourcing & Manufacturing Strategy

In case of significant changes to the Engineering technical definition between Passport 1 and 2 or if a source originally approved in the Program Sourcing Strategy changes, a sourcing re-validation is required. Depending on the parts impacted by the changes, the OPE / OPA may decide to organize a global meeting or commodity-specific reviews. The process described in section 7.3 shall be applied and the Program Sourcing Strategy form updated accordingly.

Always ensure compliance with all Contractual obligations associated to the program and to ITC restrictions.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL

Following Passport 1 review, Senior Management will approve, partially approve or reject the Dual Sourcing Strategy submitted based on the business case results and the associated risks for the program. The OPE / OPA communicates the decision to Engineering and Supply Chain and ensure that an action plan is put in place to procure and substantiate the second source parts.

In the event that other parts need to be added to the Dual Sourcing Strategy accounted for in Program CAR, the IPT will determine which business unit will absorb the costs.

Note: Please refer to OPMWI 3.10.2 Review and Validate Program Sourcing for details.

9.4 Program Operations Risks Management

Prior Passport 2, the OPE / OPA reviews, monitors and updates the Program Operations Risks list with all organizations involved. Top operational risks are communicated to Engineering during updates to the Program Risk Cube.

Note: Please refer to OPMWI 3.10.3 Manage Program Operations Risks for details.

9.5 Program Operations Level 1 & 2 Plan

The OPE / OPA updates the Program Operations Level 1 & 2 Plan shortly after Passport 1. It should be available by the time the Program CAR is approved. The template captures all activities that need to be executed or followed-up by the OPE / OPA from Passport 0 to Passport 4. It is a backbone that integrates all key industrialization topics discussed in OPMPs 3.10 and 3.11.

This plan shall be consulted and maintained on a regular basis to ensure that no key activities are missed resulting in significant delays or inefficiencies. In all cases, the OPE / OPA is free to customize the plan to fit the program needs.

Note: Please refer to OPMWI 3.10.4 Establish Program Operations Level 1 & 2 Plan for details.

This document is electronically controlled. Copies may not be the latest version.
The information contained on this page is subject to the notice set forth on the title page.
This document does not contain data subject to the EAR, the ITAR, or ECL
