Document Number:	FSW-TGE-RLPM-01
Revision Number:	1
Effective Date:	10-01-2024
Function:	RTX TE - Tech & Glbl Engineering
Authorized By:	Corporate Vice President - Global Engineering and Program Management

Functional Standard Work

Hard Copies Uncontrolled – Verify Effective Date Prior to Use

Title: RLPM Pursuit-to-Startup

Table of Contents

1. Purpose
2. Persons Responsible
3. Responsibilities
4. Process or Procedure
5. Revision History
6. Related Information
7. Change Management

1 Purpose

1.1 The purpose of this standard work is to provide additional Pursuit-to-Startup Phase requirements and details for compliance with GCP-59, RTX Lifecycle Program Management (RLPM).

2 Persons Responsible

2.1 Scope

2.1.1 The "Pursuit-to-Startup" Phase (see Figure 1) intent is to:

a. Identify potential opportunities for new and/or existing products, services, market segments,

b. Validate if the opportunity is real, determine if it is attractive and fits strategically, form the capture team, and assess if and how RTX can win it,

c. Deliver winning, executable proposals (executable = baseline Business Plan + draft lifecycle phase Management Plans),

d. Successfully negotiate contracts within approved Business Plan constraints, and

e. Transition from program capture into start-up and execution with baselined Management Plans for all lifecycle phases to follow.

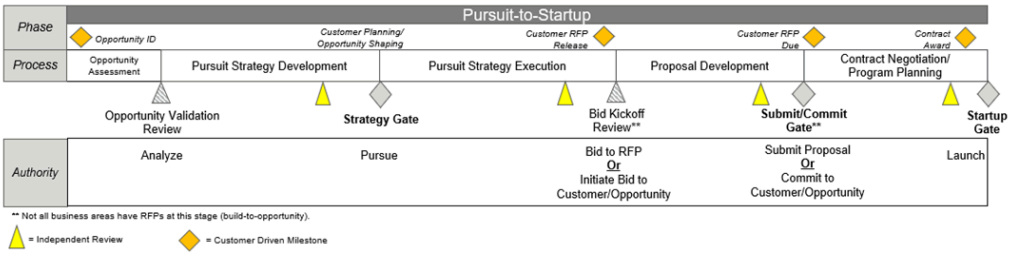

Figure 1: Pursuit-to-Startup Framework

2.1.2 Gates and Milestone Reviews Determination

a. Gates during the Pursuit-to-Startup Phase

i. Strategy Gate precedes entry into Pursuit Strategy Execution

ii. Submit/Commit Gate precedes proposal submission or submit to customer/opportunity

iii. Startup Gate occurs post Contract Award

b. Milestone Reviews during the Pursuit-to-Startup Phase

i. Opportunity Validation Review (as appropriate)

ii. Bid Kickoff Review (as appropriate as not all opportunities have Requests for Proposal (RFP) at this stage (build-to-opportunity))

2.2 Applicability

2.2.1 This standard work applies to all:

a. Organizations within RTX, including its major Business segments (each, a "**Business**"), divisions, and direct and indirect subsidiaries;

b. Majority-owned or controlled joint ventures and other majority-owned or controlled entities and operations; and

c. Directors, officers, employees, contractors, and any other persons who work for these organizations.

2.2.2 Each Business must implement the provision of this standard work within 6 months following the initial effective date. "Implement" in this context means the Business specific program lifecycle management policies are updated and released in compliance to RLPM.

2.2.3 This standard work applies throughout the RTX Lifecycle Program Management Pursuit-to-Startup Phase. See Exhibit A of GCP-59.

2.3 Persons Affected

2.3.1 This standard work applies to all stakeholders listed in the Responsible, Accountable, Support, and Inform (RASI) Matrix. See Exhibit A.

2.4 Governance

2.4.1 See FSW-TGE-0, Governance of Technology & Global Engineering Documents for governance of this FSW.

3 Responsibilities

3.1 The responsibility assignment matrix, inclusive of Responsible, Accountable, Support, and Inform, represents responsibilities for activities. For a successful RLPM, each function plays a role in meeting a requirement. See Exhibit A for the RASI that represents functional assignment recommendations.

3.2 In some cases, individuals within certain functions may perform multiple roles (for example, the Program Manager may also be the Capture Manager)

4 Process or Procedure

4.1 Requirements

4.1.1 All accountable, responsible, and support roles must participate in Gates and Milestone Reviews. See GCP-59 and Exhibit A.

a. "Responsible" is the primary point of overall responsibility

b. "Support" includes providing input/deliverables to the responsible role within each stage.

c. "Support" roles may have responsibility for sub-processes feeding into the overall process.

i. NOTE: Per GCP-59, if tailoring a Gate or Milestone Review, the Program still conducts the activities and develops the associated artifacts required in the Program Plan to meet the end objectives.

i. NOTE: For the Independent Review (IR) Framework associated with the following Gates and Milestone Reviews and for technical and strategic considerations, see Exhibit B.

ii. NOTE: See Exhibit C for recommendations associated with the Gates and Milestone Reviews.

4.1.2 Opportunity Validation Review

a. The Opportunity Validation Review must occur for new product and/or new customer/segment opportunities, as defined by the Business.

b. Each Business must establish standard criteria for reviewing and advancing all opportunities not addressed in an Opportunity Validation Review.

c. Required Exit Criteria

i. Analysis authorization or authorization to commit new business resources

ii. Assessment of ability to address intended opportunity

iii. Phase funding, schedule and team identified

iv. Preliminary Business Plan

v. IR approach

vi. Tailoring review/approval.

4.1.3 Strategy Gate

a. The Strategy Gate must occur for all competitive programs, build to market projects, or programs where business/program/technical risks are material (per Business published guidance).

b. Required Exit Criteria

i. Pursue/No pursue decision

ii. Program Management Team (PMT)/Capture team assigned

iii. Baseline capture plan as part of the Program Plan

iv. Draft Business Plan

v. Preliminary Program, Development, Production, and Sustainment Plans

vi. Phase funding, schedule and resources/investments authorized

vii. A Global Trade review conducted and baseline export/import plan, if required

viii. IRs completed per plan

ix. Tailoring review/approval

4.1.4 Bid Kickoff Review

a. Bid Kickoff Review must occur unless the Program is directly comparable to prior opportunities with the same customer and with no substantial changes or unique circumstances

i. Required Exit Criteria

1. Bid/No bid decision

2. Proposal team assigned
3. Updated capture plan as part of the Program Plan
4. Bid approach, to include:
    a. Technical baseline
    b. Bid targets and Design To Unit Production Cost (DTUPC) targets
    c. Critical items identified
    d. Technology Readiness Level (TRL)/Manufacturing Readiness Level (MRL) targets with maturation plan.
    e. Target test of reasonableness
    f. Phase funding, schedule and resources/investments authorized
5. IRs completed per plan
6. Tailoring review/approval

4.1.5 Submit/Commit Gate

a. All Programs must conduct a Submit/Commit Gate per Business requirements.
    i. NOTE: Requirements and Architecture Review may occur prior to the Submit/Commit Gate. See FSW-TGE-RLPM-02, RLPM Development for details.
    ii. Required Exit Criteria
        1. Authorization to submit/commit per Delegation of Authority (DOA)
        2. Proposal package negotiation/offer boundary conditions
        3. Bid test of reasonableness d. Baseline Business Plan
        4. Draft Program, Development, Production, and Sustainment Plans
        5. Phase funding, schedule and resources/investments authorized
        6. Management Reserve identified per GCP-59
        7. Funded TRL/MRL maturation plan i. IRs completed per plan
        8. A Global Trade review conducted and baseline or updated export/import plan, if required
        9. Tailoring review/approval
        10. Baseline Metrics Plan complete as part of the respective Management Plan for each phase

4.1.6 Startup Gate

a. Startup Gate must occur for all Programs.
b. Required Exit Criteria
    i. Authorization to launch program per DOA
    ii. Approved Program resources (finances, people, facilities/capital investment, and digital technology) to launch full development against approved Management Plans
    iii. IRs completed per plan
    iv. An updated Business Plan as necessary

v. A baseline Program Plan*

vi. A baseline Development Plan*

vii. A baseline Production Plan*

viii. 8. A baseline Sustainment Plan

ix. 9. Either an achieved TRL and MRL level required by contract and/or TRL and MRL 6, whichever is greater. If this is not achievable,

1. There must be a proposed TRL/MRL maturation plan to result in achieving TRL level 6 by Preliminary Design Review (PDR) and an MRL 6 by Critical Design Review (CDR).
2. Funding of the TRL and MRL maturation plan must occur and include back up plans if unable to achieve the proposed TRL/MRL 6 level.
3. The back up plans must meet both the Program and Business objectives

x. Confirmed Independent Research and Development (IRAD)/Contract Research and Development (CRAD) insertion and re-use assumptions with necessary updates to program cost and schedule and risk posture

xi. A Global Trade Review conducted and updated export/import plan, if required

xii. An approved architectural concept(s) baseline

NOTE: *Baseline Management Plans should be updates to draft Management Plans accounting for changes between Submit/Commit and Startup Gates. Per GCP-59, the Business defines the content of Management Plans.

5 Revision History

5.1

Rev #	Date	Content Owner	Author	Details
1.0	10.1.2024	M. Delcheccolo	C. Oban	Initial release

6 Related Information

6.1 Definitions

6.1.1 See GCP-59 for definitions of terms used within this FSW.

6.2 Acronyms

6.2.1 BOM – Bill of Material

6.2.2 CDR – Critical Design Review

6.2.3 CRAD – Contract Research and Development

6.2.4 DOA – Delegation of Authority

6.2.5 DTUPC – Design to Unit Production Cost

6.2.6 EVM – Earned Value Management

6.2.7 GRR – Global Risk Review

6.2.8 IMS – Integrated Master Schedule

6.2.9 IR - Independent Review

6.2.10 IRAD – Independent Research and Development

6.2.11 LRE – Latest Revised Estimate

6.2.12 MPS – Master Phasing Schedule

6.2.13 MR – Management Review

6.2.14 MRL – Manufacturing Readiness Level

6.2.15 PDR – Preliminary Design Review

6.2.16 PMT – Program Management Team

6.2.17 PRL – Product Readiness Level

6.2.18 PTW – Price to Win

6.2.19 RASI – Responsible, Accountable, Support, Informed

6.2.20 RFP – Request For Proposal

6.2.21 LPM – RTX Lifecycle Program Management

6.2.22 SML – Sustainment Readiness Leve

6.2.23 SRA – Schedule Risk Assessment

6.2.24 TRL – Technology Readiness Level

6.2.25 Ts&Cs – Terms and Conditions

6.3 Exhibits

6.3.1 **Exhibit A - Responsibility Assignment Matrix (RASI)**

Based on roles and responsibilities assigned within the Business, the responsible stakeholder may vary from the RASI matrix.

Stakeholders (Role) / Phase Key Processes (Culmination) **	Program Manager	Strategy	Business Development/Capture	Engineering	Operations	Supply Chain	Aftermarket/Customer Support	Quality Assurance	Legal/Contracts/Compliance	Finance	Other functional representatives, as required
Opportunity Assessment (Opportunity Validation	A	**R***	**R***	S	S	S	S	I	I	S	I
Pursuit Strategy Development (Strategy Gate)	A	S	**R**	S	S	S	S	S	S	S	I
Pursuit Strategy Execution (Bid Kickoff Review)	A	S	**R**	S	S	S	S	S	S	S	S
Proposal Development / Business Planning (Submit/Commit Gate)	**A/R**	S	S	S	S	S	S	S	S	S	S
Program Planning (Startup Gate)	**A/R**	S	S	S	S	S	S	S	S	S	S

* Per Business direction, Strategy may have responsibility for Opportunity Validation Review for new product and/or new customer/segment opportunities, while Business Development/Capture has responsibility for existing product with existing customer/segment opportunities

** Multiple functions have responsibilities leading into these Gates and Milestone Reviews that the Businesses should further define.

Legend

a. Responsible (R): Obligation to complete the deliverable or task
b. Accountable (A): Has final decision-making authority and accountability for completion of the deliverable or task
c. Support (S): Provides the support, assistance, and consultation for those responsible for the deliverable or task
d. Informed (I): Informed after a decision or action

6.3.2 Exhibit B – Independent Review (IR) Framework

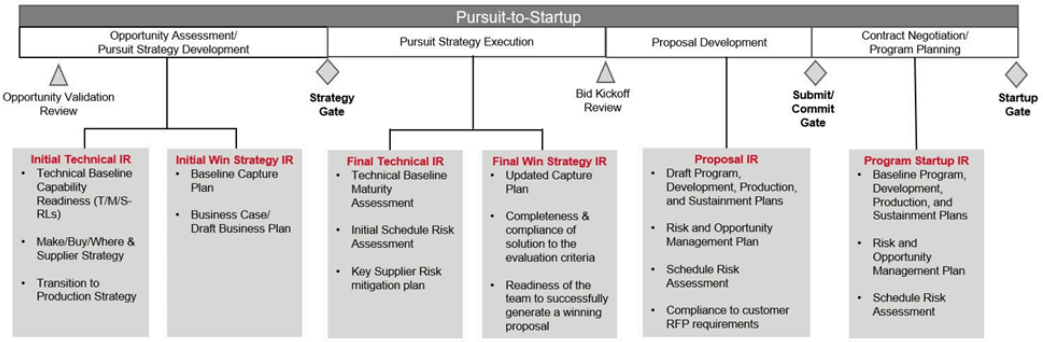

This is a recommended IR approach for a large, complex pursuit. This approach is tailorable by the Businesses based on pursuit size and archetype.

NOTE: Per GCP-59, each Business establishes policies defining the standard criteria and planned conduct of IRs within all phases. The review and approval of the IR approach for a pursuit occurs as part of the Opportunity Validation Review.

6.3.3 Exhibit C – RecommendedEntrance Criteria and Content that Should Lead Into Gate or Milestone Review

Major Processes	Opportunity Assessment	Pursuit Strategy Development	Pursuit Strategy Execution	Proposal Development/ Business Planning	Contract Negotiation/ Program Planning
Entrance Criteria	New Opportunity Identified for Consideration	• Approval of Prior Gate/Review • Review of Tailoring/ Waivers	• Approval of Prior Gate/Review • Review of Tailoring/ Waivers	• Approval of Prior Gate/Review • Review of Tailoring/ Waivers	• Approval of Prior Gate/Review • Review of Tailoring/ Waivers
Activity/ Content	• Opportunity Assessment • Competitive Assessment • Strategic Fit Assessment • Cross RTX Partnership Assessment • Customer Engagement Plan • Sales Intermediary (rep or consultant) Plan • Market Validation Plan • Plan ($, resources, tasks) to get to Strategy Gate • Initial Global considerations – release, EXIM, Offset/ Industrialization, Global Trade/ Initial Global Risk Review (GRR) • Risk & Opportunity Analysis/ Closure Plan	• Opportunity Overview • Business Case • Addressed Segment/ Customer Analysis • Capture Team Staffing • Operational Analysis • Win Strategy (including PTW) • Technical Baseline • Capability Readiness (T/M/S-RLs) • Transition to Production Strategy • Make/Buy/Where Analysis & Supplier Strategy • Investment Requirements • Release and Licensing Reqts • Offset/ Industrialization Plan • Global Trade/GRR • Staffing/Legal Considerations • Legal Entity and Deployment Requirements • Risk & Opportunity Analysis/Closure Plan	• RFP Summary • Updated Win Strategy (including Price to Win) • Assumptions: Internal/External • Requirements definition maturity • Technical Approach/ Bid BOM • DTUPC • Key Lifecycle Considerations • Bid Approach & Key Assumptions • TINA Compliance Plan (if applicable) • Export Tax, Bond, & Foreign Exchange Requirements • Work Breakdown Structure and Responsibility Assignment Matrix • Data Rights & IP Strategy • Offset/ Industrialization Plan • Global Trade/GRR • Risk & Opportunity Analysis/ Closure Plan	• Opportunity & Strategy Update • Key Ts & Cs (Customer & Suppliers), Reqts Exceptions • Updated Assumptions • Win Assessment • Technical Approach/ Bid BOM • Contract Closure Plan • Financials, including MR Approach • Execution Overview • Readiness Assessment • Supplier Alignment Risk Mitigation • Bid to Startup Plan • Negotiation Strategy • Offset/ Industrialization Plan • Global Trade/GRR, Product Safety, Cybersecurity & Security Considerations • MPS and high-level IMS • EVM and LRE approach • Risk & Opportunity Analysis/Closure Plans – Phase	• Baseline Business Plan Update • Contract walk-through (PMT, customer, suppliers) • BOM Maturity Assessment/Update (Critical component suppliers, long lead, subcontracted components secured with flow downs) • TRL/MRL/ PRL(Product)/SRL Assessment • Project Complexity Assessment • Completed Stakeholder Requirements Review • Offset Plan (if applicable) • Risk & Opportunity Analysis/Closure Plan • Robust IMS + SRA • Performance Measurement Baseline • Aligned Staffing ramp plan • Program cadence • Metrics & Technical Performance Measures Plan
Gate/ Milestone Review	Opportunity Validation Review (Is it Real?)	Strategy Gate (Can we Win?)	Bid Kickoff Review (Can we Meet Reqts?)	Submit/Commit Gate (Is it Worth It?)	Startup Gate (Are we ready to execute?)

6.4 Links to reference material

6.4.1 GCP-59 RTX Lifecycle Program Management

6.4.2 FSW-TGE-0 Governance of Technology & Global Engineering Documents

6.4.3 FSW-TGE-RLPM-02 RLPM Development

6.4.4 FSW-OPSC-RLPM-03 RLPM Production

6.4.5 FSW-TGE-RLPM-04 RLPM Sustainment

7 Change Management

7.1 Communication, awareness and access to the FSW are key to success.

7.1.1 Communicate and train employees to perform tasks as defined in the FSW.

7.1.2 Post the FSW in a location accessible by all impacted persons (Examples include SharePoint Online, Teams, and ePolicy).

7.1.3 Periodically review and update the document to incorporate improvements.
