Document Number:	GCP-59
Revision Number:	0.4
Effective Date:	10-01-2024
Function:	RTX TE - Tech & Glbl Engineering
Authorized By:	Senior Vice President - Technology and Global Engineering

General Corporate Policy

Hard Copies Uncontrolled – Verify Effective Date Prior to Use

Title: RTX Lifecycle Program Management

Table of Contents

1. Purpose
2. Persons Affected
3. Responsibilities
4. Policy
5. Revision History
6. Related Information
7. Exhibits

1 Purpose

1.1 To govern the RTX Corporation (the "**company**") product lifecycle management process for planning and execution of programs or the management of products, programs, and/or services across the lifecycle using the RTX Lifecycle Program Management (RLPM) framework defined within this policy.

1.2 The RLPM framework is RTX's method for evaluating, selecting, and managing the capture and execution of programs, products, and/or services from inception, to capture, through development, production, and sustainment until the product is out of service.

2 Persons Affected

2.1 This policy applies to all:

2.1.1 Organizations within RTX, including its major business segments (each, a "**Business**"), divisions, and direct and indirect subsidiaries;

2.1.2 Majority-owned or controlled joint ventures and other majority-owned or controlled entities and operations; and

2.1.3 Directors, officers, employees, contractors, and any other persons who work for these organizations.

2.2 Exceptions granted to any of the above must comply with the requirements of GCP-0, Issuance and Maintenance of Corporate Policies.

2.3 Each Business must implement the provisions of this policy within 6 months following the initial effective date. "Implement" in this context means the Business specific program lifecycle management policies are updated and released in compliance to RLPM.

3 Responsibilities

3.1 Each Business must issue a specific program lifecycle management policy in compliance with this policy and related Functional Standard Work (FSW) for the planning and execution of Program capture and execution appropriate for the respective Business. See definition in Exhibit B.

3.2 Each Business must:

3.2.1 Require the use and maintenance of RLPM as shown in Exhibit A as their Business lifecycle management framework for implementation and tailoring for a Program. This includes this policy and the four related FSWs (FSW-TGE-RLPM-01, FSW-TGE-RLPM-02, FSW-OPSC-RLPM-03 and FSW-TGE-RLPM-04).

a. Establish tailoring requirements and approvals for the RLPM process. See Tailoring sections in paragraph 4.2.

3.2.2 Integrate and maintain RLPM processes into Business level policy documents.

3.2.3 Maintain, revise, and update RLPM processes to incorporate continuous improvement in business capture and execution of programs.

3.3 All individuals who access RLPM policy documents must protect them in accordance with GCP-14, Protection of RTX and Third Party Information.

3.4 Employees assigned as Program Managers must establish continuity across the lifecycle of the program, product, and/or service offering. See Section 7.3, Exhibit C - Responsibility Assignment Matrix (RASI). The Program Manager must:

3.4.1 Lead a Program Management Team (PMT) through gates and milestone reviews.

3.4.2 Maintain accountability and authority over all RLPM phases of a given program, product, and/or service and related investment commitments.

3.4.3 Maintain accountability to the external customer(s) on behalf of the Company.

3.4.4 Adhere to phase specific requirements within the RLPM FSWs (FSW-TGE-RLPM-01, FSW-TGE-RLPM-02, FSW-OPSC-RLPM-03 and FSW-TGE-RLPM-04).

3.5 For successful RLPM, the Program Manager must establish a cross-functional PMT. Exhibit C defines each function's role which assigns the stakeholder roles of Responsible, Accountable, Support, and Informed (RASI) for each lifecycle phase. These represent functional assignment recommendations. See Exhibit D for description of PMT potential members.

4 Policy

4.1 Each Business must:

4.1.1 Develop, deploy, and maintain the RLPM process for the Business planning and execution of programs aligned to Exhibit A, ensuring that the process defines:

a. The entire lifecycle from Program pursuit-to-startup, development, production through sustainment inclusive of product delivery and service/support. Business RLPM processes must be consistent with Business Quality requirements, any associated contract requirements, and this policy inclusive of referenced FSW.

b. The roles and responsibilities associated with the RLPM process. See Exhibits C and D.

4.1.2 Measure process maturity of its product development and service delivery capabilities, consistent with RTX Customer Oriented Results & Excellence ("**CORE**") Operating System and/or contractual requirements.

4.1.3 Develop an individual RASI that further addresses the steps within each of the Pursuit-to-Startup processes aligned to the specific organizational structure. Businesses should designate the individual who has customer interfacing responsibility.

4.1.4 Determine gate and milestone review approval level by existing Business Delegation of Authority (DOA).

4.1.5 Establish a standard set of metrics per function for each phase for use by Programs based on Business established criteria.

4.2 RLPM Implementation (see Exhibit B for definitions)

4.2.1 Framework: The framework consists of four distinct phases that leverage functional responsibilities of key performing functions, a gated approval process, and a distinct set of milestone reviews across the lifecycle. The four phases are Pursuit-to-Startup, Development, Production, and Sustainment. There may be activities before the phase that are concurrent with another phase. See Exhibit A. Each phase of the lifecycle has clear entrance and exit criteria, key processes, metrics, and defined

deliverables. See the respective FSW per phase. All Businesses, functions, and Programs must use their RLPM process framework per this policy, the FSW per phase per Related Information, and their Business specific implementation policies.

4.2.2 Gate: The RLPM must execute to defined gates and identify the appropriate level of approval authority based on Business criteria. The Business must not add additional gates. As a result of the gate, the Program Manager must ensure capture of a documented decision. The gates include:

a. Strategy (Gate A)

b. Submit/Commit (Gate B)

c. Startup (Gate C)

d. Production Readiness (Gate D)

e. Production Closure/Field Support (Gate E)

f. Discontinuation of Support (Gate F)

4.2.3 Milestone Review: The RLPM must execute defined milestone reviews at key points within each lifecycle phase. See Exhibit A. Businesses may add additional reviews as applicable. See the applicable FSW for the different milestone reviews. The Business must define criteria and level of approval authority required for each defined milestone review. The milestone review must:

a. Assess opportunity, bid kickoff, technical solution maturity, production process validation, manufacturing performance, and/or sustainment product support.

b. Assess that the appropriate mitigation plans are in place for risks.

c. Make go/no-go decisions to proceed to next major activities.

d. When there is a material impact from a milestone review, trigger a delta gate review (from last approved gate) and/or an escalation review based on threshold established by the Businesses.

e. Businesses should:

i. Tailor milestone reviews based on predefined criteria approved by the Business.

ii. Establish requirements for additional milestone reviews between gates, such as post Critical Design Review.

4.2.4 Independent Review: Each Business must establish requirements for the conduct of independent reviews to occur. Each Business must establish standard criteria for the conduct of independent reviews such as significant program scope change, changes to contract terms and conditions, technical complexity, or risk profile.

4.2.5 Cadence Review: Each Business must establish the requirements for effective Program cadence reviews based on business criteria.

4.2.6 Supplemental Review: Each Business must define the criteria for supplemental reviews such as a Make/Buy/Where Review within the Production Phase.

4.2.7 Management Plans: Each Business must define the required contents for each management plan listed below. The management plan maturity level is based on program, product, or service as applicable for each phase. See Exhibit A for timing and Exhibit B for definitions. See GUI-TGE-RLPM-001, RLPM Management Plan Content Recommendations for suggested sections.

a. Business Plan

b. Program Plan

c. Development Plan

d. Production Plan

e. Sustainment Plan

4.2.8 Tailoring Applicability: The intent of the tailoring process is to remove parts of the RLPM that are not necessary because that scope is not applicable to the Program lifecycle. The intent of tailoring is to adapt scope for project specifics and limited to what is applicable to the Program lifecycle. See GUI-TGE-RLPM-002, RLPM Tailoring Examples for reference.

a. Each Business must establish tailoring criteria for Business specific programs, projects, and/or contracts.

b. Each Business should define Business specific archetypes, with associated tailoring, to facilitate more efficient tailoring at the Program level. This includes management plan applicability.

c. If the Program tailors out a gate or milestone review, the Program must still conduct the activities and associated artifacts required in the Program Plan to meet the end objectives.

d. RLPM activities beyond the contract scope must be in the Program Plan and include associated funding. If tailoring downstream deliverables, the gate approval authority and impacted function(s) must approve the RLPM tailoring. For example, development contract to include activities during development required for production readiness.

e. The Program Plan must include a tailoring plan that meets all the tailoring requirements outlined in this policy.

4.2.9 Tailoring approval: Each Business must establish an approval process that assures tailoring approval for projects and/or contracts.

a. Gate approval authority must approve the tailoring that includes sign off by all key stakeholders with concurrence from impacted function(s).

b. Concurrence from impacted function(s) must come from the cognizant Business functional leader. The Business functional leader may delegate the functional approval authority for lower level gate reviews.

c. Each Business must establish and maintain separate definitions for large, complex, and strategic Programs.

d. Each Business must establish additional approval criteria for an independent review team to approve tailoring for large, complex, and strategic Programs as defined in their policies.

e. The Program Manager must ensure tailoring of requirements occur to align with the Contract or Statement of Work <u>and</u> this policy. The Program Manager must document Tailoring decision rationale.

4.2.10 RLPM Waivers: If a Business does not meet or plan to meet an applicable RLPM requirement, or a customer requirement stipulates an alternate approach, an

RLPM waiver is mandatory. Approval of RLPM waivers must follow the same process outlined in section 4.2.9.a and 4.2.9.b.

4.3 Program Management Team (PMT)

4.3.1 The Program Manager must be the leader of an integrated program management team through all gates and milestone reviews and decision making for all customer and/or investment commitments.

4.3.2 The Program Manager must be accountable and have authority, subject to the limits of his/her position, over all RLPM phases of a given Program.

4.3.3 The Program Manager must be accountable to the customer(s) on behalf of the PMT.

4.3.4 The Program Manager must ensure the composition of the cross-functional team includes representatives from the functional organizations required to support all phases of the Program lifecycle. See Exhibits C and D for potential functions.

4.3.5 The respective functions should empower PMT Leads to represent and make commitments within the scope of the Program on the functions' behalf aligned to the RASI in Exhibit C and the phase RASIs.

4.3.6 During the Pursuit-to-Startup Phase, the PMT shapes, formulates, and executes the capture strategy throughout the lifecycle of the program, product, and/or service offering.

a. The PMT must ensure the capture strategy for the pursuit accounts for customer requirements and aligns with the Business level Long Range Plan (LRP) and Business Plan and this policy including all referenced FSWs. See Exhibit A for all management plans and timing as it relates to the phases.

b. The capture strategy must include the systematic capture of customer feedback and execution of market research. Use this information to develop and refine the Program Business Plan.

4.3.7 The PMT must develop management plans as applicable for the Program. The PMT must have management plans approved at the given gate per the maturity specified in Exhibit A. This includes:

a. Establishment of management plans, as applicable for the program, and

b. Ensuring the management plans are at the appropriate maturity level for a given gate for approval.

4.3.8 When managing requirements, the PMT manages scope and controls change across the lifecycle of the Program. The PMT must:

a. Flow down all requirements (regulatory, technical, contract, and this policy including all referenced FSWs), both internally to Program team members and externally to the supply base, and ensure compliance.

b. Establish and maintain program level change control process to disposition proposed scope/requirements changes (both internal and external) that drive cost or schedule impacts, chaired by the Program Manager or delegate(s), immediately following the Submit/Commit Gate.

4.3.9 When conducting planning, the PMT must use executable schedules across the lifecycle of the Program. This includes establishing an executable master schedule and maintaining it as appropriate throughout the Program.

4.3.10 The Program Manager must ensure establishment and maintenance of a Program cadence across the lifecycle of the Program. This must include periodic Program reviews to monitor program health and status. This may include initiating appropriate corrective action. The gate approval authority must approve the Program review cadence as documented in the Program Plan.

4.3.11 The PMT must own Risk and Opportunity (R&O) and Management Reserve (MR) across the lifecycle of a Program.

a. The PMT must establish and maintain an R&O process and cadence throughout the lifecycle and communicate significant changes to impacted stakeholders per the Program Plan.

b. The Program Manager must ensure the review and update of the R&O register per the established program calendar.

c. The Program Manager must establish MR no later than Submit/Commit Gate based on the R&O Profile, and revisit and baseline the MR prior to the Startup Gate.

d. If an appropriation request is required in accordance with FCP-FIN-ACC-28.01, Appropriation Requests, the R&O profile and resulting MR must be consistent with the Submit/Commit Gate.

4.3.12 The PMT must document authorization and commitments using the gate process across the lifecycle of the Program.

a. The PMT must follow a gated review process to document Program Manager and team authorization and commitment to proceed through a given gate and into the next phase of the Program.

b. Delta gates must occur when an event impacts the team's ability to meet the Business Plan or current commitments.

c. The Program Manager is accountable and must ensure all contract closure requirements are complete.

4.3.13 PMT must use metrics against major commitments to allow early detection of risks and take action to mitigate the risks across the lifecycle of the Program. The PMT must:

a. Establish a metrics plan as part of the respective phase management plan for each phase of RLPM, capturing current status against major commitments such as safety, customer, technical, programmatic, LRP, business plan, and/or annual plan. The metrics plan includes Leading Indicator (LI) metrics for each phase. See Exhibit E for examples.

b. As part of a Development Phase, the minimum established program metrics to monitor program performance are:

i. Schedule performance (actual vs plan & forecast),

ii. Cost performance (actual vs plan & forecast), and

iii. MR (actual vs plan & forecast) and sufficiency based on R&O Profile.

4.3.14 The PMT must use the CORE goal alignment methodologies to ensure capture and execution strategies align with Business goals across the lifecycle of the Program.

5 Revision History

5.1 This policy supersedes FCP-TGE-004, Product Development Process for Planning and Execution, effective March 29, 2021.

5.2 Administrative/Immaterial revisions include:

5.2.1 (Rev 0.1) Link updated in Section 6.3 (11/5/24).

5.2.2 ePolicy links updated (12/18/25)

5.2.3 Updated graphic for Exhibit A (1/28/26).

5.2.4 Updated link to GUI-TGE-RLPM-001 in Section 6.3 (2/12/26).

6 Related Information

6.1 General Corporate Policies (GCP)

GCP Doc Number	General Corporate Policy Title
GCP-0	Issuance and Maintenance of Corporate Policies
GCP-14	Protection of RTX and Third Party Information

6.2 Functional Corporate Policies (FCP)

FCP Doc Number	Functional Corporate Policy Title
FCP-FIN-FPA-28.01	Appropriation Requests

6.3 Additional Related Information

Related Document	Related Document Title
FSW-TGE-RLPM-01	RLPM Pursuit-to-Startup

FSW-TGE-RLPM-02	RLPM Development
FSW-OPSC-RLPM-03	RLPM Production
FSW-TGE-RLPM-04	RLPM Sustainment
GUI-TGE-RLPM-001	RLPM Management Plan Content Recommendation
GUI-TGE-RLPM-002	RLPM Tailoring Examples

7 Exhibits

7.1 Exhibit A – RTX Lifecycle Program Management Framework

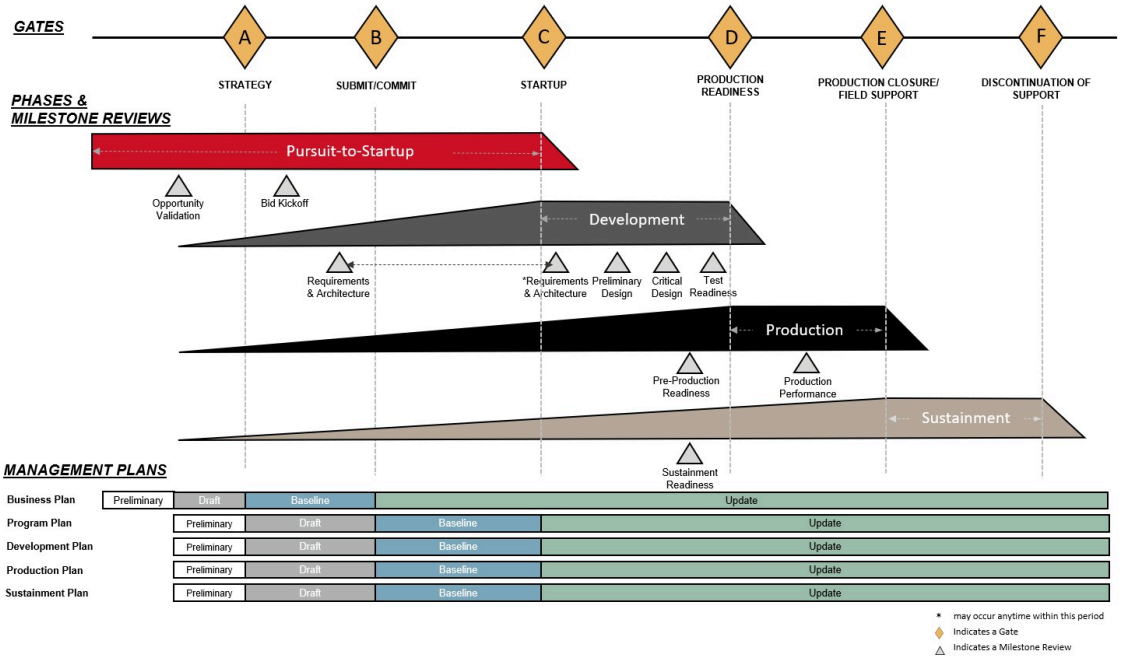

7.2 Exhibit B - Definitions

7.2.1 Archetype: A defined grouping of like Programs to accelerate tailoring for a type of contract applicability considering potential future scope such as production or sustainment. Some examples of archetypes include similar quality requirements,

engineering challenges, complexity, risk, applicable phase, large/complex/strategic, or contract type (such as Department of Defense contract, direct commercial sales contract, or contracts with offset requirements).

7.2.2 Cadence Review: Ensure appropriate communication and coordination exists within the PMT, across the various levels of leadership that have overarching accountability and responsibility for the Programs, and with those organizations responsible for aggregating performance of the business.

7.2.3 Contract: Any legally binding agreement undertaken by the company to sell, lease or license goods, services or intellectual property to an external customer. This definition includes, but not limited to, sales contracts (including undefinitized or letter contracts), bilateral agreements, subcontracts or purchase orders, pro-forma invoices, basic ordering agreements, Cooperative Research and Development Agreements (CRADAs) and license agreements, notices of award or a written authority to proceed, including amendments and modifications thereto; wherein the customer, either a government or commercial company, requests that RTX commence performance of a proposed effort and obligates itself, without contingencies, to the financial arrangement stated in the agreement.

7.2.4 Gate: Decision points within the Program lifecycle around major investments (as determined by the Business) and/or commitments to a customer; the transition of primary functional responsibility within the lifecycle, or an event that affects the ability to meet Business Plan commitments. Gates have a defined set of key stakeholders required for review and approval. (See the six defined gates in Exhibit A)

7.2.5 Independent Review: A systematic review of program, product maturity, service, and process compliance performed by a team of subject matter experts (SMEs) who are not part of the execution team during the lifecycle.

7.2.6 Lifecycle: A standard, common, and disciplined approach to manage the program, product, and/or service through the phases of the framework.

7.2.7 Material Impact: Business case change such as cost overrun, major schedule slip, or major changes to risk profile

7.2.8 Milestone Review: Defined major milestones associated with each lifecycle phase. There may be a series of reviews within a phase.

7.2.9 Phase: Major section of the lifecycle with clear entrance/exit criteria, key processes and roles and responsibilities RASI (responsible, accountable, support, informed) matrix.

7.2.10 Plan Maturity Level: A description of the maturity of the plan throughout the phases. These include preliminary (initial creation), draft (update), and baseline (for continued execution).

7.2.11 Program: A product or service which is delivered to an external customer; a finished subassembly, product, or service which is delivered to a program for integration; or a portfolio of efforts that may include multiple contracts representative of different phases. Program is inclusive of programs, products, and services.

7.2.12 Program Management Team (PMT): Composed of the functional or product leads that manage the required resources necessary to plan, execute, and manage the

Program through the lifecycle.

7.2.13 RLPM Waiver: A specific written authorization for an exception from specific RLPM requirements driven by a formal customer request to remove the scope proposed or the Program's inability to meet the requirement.

7.2.14 Tailoring: Removes elements (phase, gate, milestone reviews, and/or requirements) of the framework that are not applicable to a Program's lifecycle.

7.3 Exhibit C - Responsibility Assignment Matrix (RASI)

7.3.1 Based on roles and responsibilities assigned within a Business, the responsible stakeholder in the Business may vary from this RASI matrix.

Stakeholders (Role) / Phase or Key Deliverable	Program Manager	Strategy	Business Development/Capture	Engineering	Operations	Supply Chain	Aftermarket/Customer Support	Quality Assurance	Legal/Contracts/Compliance	Finance	Other functional representatives, as required
Program Management	A/R	S	S	S	S	S	S	S	S	S	S
Pursuit-to-Startup Phase	A*	S	R	S	S	S	S	S	S	S	S
Development Phase	A	I	I	R	S	S	S	S	S	S	S
Production Phase	A	I	I	S	R	S	S	S	S	S	S
Sustainment Phase	A	S	S	S	S	S	R	S	S	S	S

*Program Manager is responsible (R) at Startup Gate

7.3.2 Legend

a. Responsible (R): Obligation to complete the deliverable or task

b. Accountable (A): Has final decision-making authority and accountability for completion of the deliverable or task, subject to the limits of his/her position

c. Support (S): Provides the support, assistance, and consultation for those responsible for the deliverable or task

d. Informed (I): Informed after a decision or action

7.4 Exhibit D - Stakeholder Roles and Responsibility Description for Each FSW

7.4.1 Program Manager: Accountable for delivering a program, product, or service; business performance; gate approvals; and customer commitments across the full lifecycle in accordance with this policy including all referenced FSWs.

7.4.2 Strategy: Responsible for market analysis, strategic planning, and evaluating strategic fit of new opportunities.

7.4.3 Business Development: Responsible for the identification and capture of business opportunities including providing the voice of the customer and support of strategic and financial planning throughout the product lifecycle.

7.4.4 Engineering: Responsible for the engineering activities to design and deliver safe, technically compliant and producible products and/or services in accordance with

customer requirements and this policy including all referenced FSWs within the allocated budget and schedule.

7.4.5 Operations: Responsible for successful execution of tasks related to manufacturing and delivery of products throughout the lifecycle of the program and ensures the alignment between manufacturing and supply chain. Ensures efficient production processes, capacity, quality control, safety, and adherence to cost targets.

7.4.6 Supply Chain: Responsible for supply chain strategy, collaborating with Engineering and Operations on definition and release of hardware/software and services in alignment with the program requirements and acquisition schedule needs including supplier selection and risk management. Ensures timely delivery, availability of resources, and mitigation of supply chain material flow disruptions.

7.4.7 Aftermarket/Customer Support: Responsible for aftermarket activities including resources, schedules and priorities, technical support and monitoring of reliability and product improvements, to ensure program requirements are met.

7.4.8 Quality Assurance: Responsible for the execution of the Quality Assurance Plan and successful execution of quality deliverables. Ensures the identification, flow down, and adherence to all customer and industry quality requirements and standards.

7.4.9 Legal/Contracts/Compliance: Leads with applicable negotiations, supports interpretation and coordination of the contract, responsible for providing guidance regarding contractual coverage, compliance with regulations, global trade requirements, intellectual property, this policy including all referenced FSWs, and requirements flow down.

7.4.10 Finance: Responsible for program financials by analyzing and providing financial data that is accurate, timely, and in accordance with internal and contractual policies.

7.4.11 Other functions, as needed:

a. Digital Technology: Responsible to support the program with the digital tools required to capture and execute programs.

b. Human Resources: Responsible to support the program to fill staffing requirements.

c. Safety (Product/System): Responsible to support all functions to ensure the safety and well-being of the end user and team involved in the design and development phase.

7.5 Exhibit E – Example Measures per Phase

Phase/Type	Quality	Technical	Cost	Schedule	Other
Pursuit-to-Startup		Requirements traceability	P(win) vs P(go) trends	Schedule risk assessment	Risk/Opportunity Indicator Indices
		Requirements volatility	Bid/Design to Cost estimate vs targets		
			Cost roll up minus proposal price		
			% Firm supplier quotes		

Phase/Type	Quality	Technical	Cost	Schedule	Other
Development	Defect Density/Failure Malfunctions	Requirement Burn down (progress of technical verification or completion to plan)	Cost Variance (Total Delta of Budget to Actual Cost)	Schedule Variance (Total Delta of Planned Schedule to Actual Schedule)	# of Safety Boards/ Assessments Conducted
	Defects in a product relative to size			Schedule Efficiency (similar to cost is it taking you more time or less to complete per task)	
			Cost Efficiency (Assessment of are you aligned with your expected burn rate (is it costing you more or less per task)	Schedule KPIs aligned with PM Schedule KPIs	
			Cost KPIs aligned with PM Cost KPIs		
Production	Critical Items & Key Product Characteristics (KPC) (including product safety) Identified	Changes Post Production Readiness (out of phase) – reason and # (Supplier, Process, Engineering)	Productivity	Capacity model (Throughput, Yield, Spares, Repairs)	AS9145 Adoption (Advanced Program Quality Planning)% of applicable elements adopted
	Process Capability of KPCs	Producibility Incorporation (Design Failure Mode and Effects Analysis, Process Failure Mode and Effects Analysis,, Design for Manufacturing Assembly)			

Phase/Type	Quality	Technical	Cost	Schedule	Other
Sustainment	Mean Time Between Failures/Mean Time Between Unscheduled Removal/Software (SW) failures	# of Notice Of Escapes	Warranty/support costs	Spares/Service parts/SW On Time Delivery	Customer surveys
	Out of box failure (DOA)/ Installation failures	*# of safety events	Cost to Repair – required if HW	Turn Around Time (TAT) - if Hardware (HW)	
	No Fault Found (HW)/No issue found (SW)		Net Asset cost compared to plan – required if HW	Repair Work in Process backlog	
	Audit Findings/Corrective Action Requests		Cost of poor quality		
